

INSTALL

P38

1 × Building 6m → Green Room 1

DATE	Mon 28 Sep 2026	
TRUCK LEAVES	09:00	Kingston
CARRIER	SFL	
ON SITE	After 07:00	
LOAD	One truck · one ref	

ON THE TRUCK

WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
1 × Building 6m Green Room 1 · Portable buildings	1327218	☐ Fridge (Full Size)

WHERE IT GOES

LOCATION	Green Room 1	
SECTOR		CALLOUT
NEXT TO	STAGE	BESIDE P39, P42
NEAR	Macintosh Island (~75 m)	DOOR FACES



MASTER-PLAN POSITION
-27.984590, 153.427601
From master plan D001 · not a
phone pin
SCAN TO NAVIGATE

PHOTOS



Master plan



Close-up



Around it



The product · stock photo

INSTALL LIST

- | | | |
|---|--|---|
| ☐ Unload a building (crane) | ☐ Position and level a building | ☐ Blocks and packers under skids |
| ☐ Fit stairs and landings | ☐ Power-on check with the electrician | ☐ Forklift work |
| ☐ Spotting | ☐ Arrival recorded in the page | ☐ Photos uploaded to the page |
| ☐ Asset numbers recorded in the page | | |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher 0429 352 788 INSTALLER Aaron Zelvis 0429 493 057 INSTALLER Alfie Harris 0403 149 326
INSTALLER Kyle Gover 0403 789 142 IEDM SAFETY & TRAFFIC Steve Haines 0407 734 398 IEDM SITE MANAGER John Brett 0433 809 117 EMERGENCY 000

INSTALL

P39

1 × Building 6m → Green Room 2

DATE	Mon 28 Sep 2026	
TRUCK LEAVES	09:30	Kingston
CARRIER	SFL	
ON SITE	After 07:00	
LOAD	One truck · one ref	

ON THE TRUCK

WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
1 × Building 6m Green Room 2 · Portable buildings	1327216	☐ Fridge (Full Size)

WHERE IT GOES

LOCATION	Green Room 2	
SECTOR		CALLOUT
NEXT TO	STAGE	BESIDE P38, P42
NEAR	Macintosh Island (~75 m)	DOOR FACES



MASTER-PLAN POSITION
-27.984640, 153.427550
From master plan D001 · not a
phone pin
SCAN TO NAVIGATE

PHOTOS



Master plan



Close-up



Around it



The product · stock photo

INSTALL LIST

- | | | |
|---|--|---|
| ☐ Unload a building (crane) | ☐ Position and level a building | ☐ Blocks and packers under skids |
| ☐ Fit stairs and landings | ☐ Power-on check with the electrician | ☐ Forklift work |
| ☐ Spotting | ☐ Arrival recorded in the page | ☐ Photos uploaded to the page |
| ☐ Asset numbers recorded in the page | | |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher 0429 352 788 INSTALLER Aaron Zelvis 0429 493 057 INSTALLER Alfie Harris 0403 149 326
INSTALLER Kyle Gover 0403 789 142 IEDM SAFETY & TRAFFIC Steve Haines 0407 734 398 IEDM SITE MANAGER John Brett 0433 809 117 EMERGENCY 000

INSTALL

P42

1 × Building 6m → Production

DATE	Mon 28 Sep 2026	
TRUCK LEAVES	10:00	Kingston
CARRIER	SFL	
ON SITE	After 07:00	
LOAD	One truck · one ref	

ON THE TRUCK

WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
1 × Building 6m Production · Portable buildings	1327221	☐ Fridge (Full Size)

WHERE IT GOES

LOCATION	Production	
SECTOR		CALLOUT
NEXT TO	STAGE	BESIDE P38, P39
NEAR	Macintosh Island (~75 m)	DOOR FACES



MASTER-PLAN POSITION
-27.984541, 153.427654
From master plan D001 · not a
phone pin
SCAN TO NAVIGATE

PHOTOS



Master plan



Close-up



Around it



The product · stock photo

INSTALL LIST

- | | | |
|---|--|---|
| ☐ Unload a building (crane) | ☐ Position and level a building | ☐ Blocks and packers under skids |
| ☐ Fit stairs and landings | ☐ Power-on check with the electrician | ☐ Forklift work |
| ☐ Spotting | ☐ Arrival recorded in the page | ☐ Photos uploaded to the page |
| ☐ Asset numbers recorded in the page | | |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher 0429 352 788 INSTALLER Aaron Zelvis 0429 493 057 INSTALLER Alfie Harris 0403 149 326
INSTALLER Kyle Gover 0403 789 142 IEDM SAFETY & TRAFFIC Steve Haines 0407 734 398 IEDM SITE MANAGER John Brett 0433 809 117 EMERGENCY 000

INSTALL · 3 REFS

GN01

60kva

WC01

Accessible Toilet, FWF

WC42

FWF

DATE	Mon 28 Sep 2026	
TRUCK LEAVES	10:30	Kingston
CARRIER	SFL BOGIE	
ON SITE	After 07:00	
LOAD	One truck · 3 refs · same time and carrier	

ON THE TRUCK

REF	WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
GN01	1 × 60kva Generator · Generators	1261271	None on the schedule
WC01	1 × Accessible Toilet · 2 × FWF Toilets · Toilets & amenities		None on the schedule
WC42	1 × FWF Toilets · Toilets & amenities		None on the schedule


WHERE IT GOES

REF	LOCATION	CALLOUT	NEXT TO · BESIDE	POSITION	NAVIGATE
GN01	Generator Sector S13	001 D024-26003-02	BS01	-27.985974, 153.426924 From master plan D001 · not a phone pin	
WC01	Toilets Sector S10	WC01 D023-26003-02	OP08, OP21	-27.983425, 153.425250 From master plan D001 · not a phone pin	
WC42	Toilets Sector S10	WC42 D023-26003-02		-27.983295, 153.424824 From master plan D001 · not a phone pin	

PHOTOS




Every unit on this load

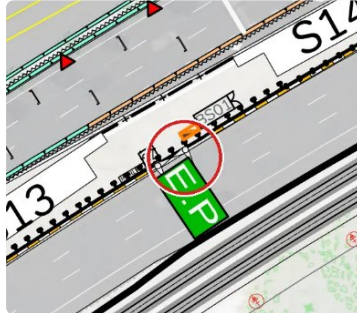

GN01 Master plan



WC01 Master plan

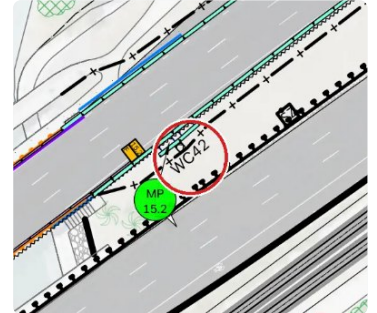

WC42 Master plan

INSTALL LIST

- | | | |
|---|---|--|
| ☐ Unload portaloos WC01, WC42 | ☐ Power-on check with the electrician GN01 | ☐ Forklift work |
| ☐ Spotting | ☐ Arrival recorded in the page | ☐ Photos uploaded to the page |
| ☐ Asset numbers recorded in the page | | |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher 0429 352 788 INSTALLER Aaron Zelvis 0429 493 057 INSTALLER Alfie Harris 0403 149 326 INSTALLER Kyle Gover 0403 789 142
IEDM SAFETY & TRAFFIC Steve Haines 0407 734 398 IEDM SITE MANAGER John Brett 0433 809 117 EMERGENCY 000

INSTALL

P06

1 × Building 6m → Wilclean Crib Room

DATE	Mon 28 Sep 2026	
TRUCK LEAVES	10:30	Kingston
CARRIER	SFL	
ON SITE	After 07:00	
LOAD	One truck · one ref	

ON THE TRUCK

WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
1 × Building 6m Wilclean Crib Room · Portable buildings	1097453	☐ Fridge (Full Size) ☐ Zip Boiler ☐ Sink w Tap ☐ Microwave

WHERE IT GOES

LOCATION	Wilclean Crib Room	
SECTOR		CALLOUT 006 on D022-26003-02
NEXT TO	WIL	BESIDE
NEAR	Macintosh Island (~70 m)	DOOR FACES



MASTER-PLAN POSITION
-27.984233, 153.427739
From master plan D001 · not a phone pin
SCAN TO NAVIGATE

PHOTOS



Master plan



Close-up



Around it



The product · stock photo

INSTALL LIST

- | | | |
|---|--|---|
| ☐ Unload a building (crane) | ☐ Position and level a building | ☐ Blocks and packers under skids |
| ☐ Fit stairs and landings | ☐ Power-on check with the electrician | ☐ Forklift work |
| ☐ Spotting | ☐ Arrival recorded in the page | ☐ Photos uploaded to the page |
| ☐ Asset numbers recorded in the page | | |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher 0429 352 788 INSTALLER Aaron Zelvis 0429 493 057 INSTALLER Alfie Harris 0403 149 326 INSTALLER Kyle Gover 0403 789 142
IEDM SAFETY & TRAFFIC Steve Haines 0407 734 398 IEDM SITE MANAGER John Brett 0433 809 117 EMERGENCY 000

INSTALL

WC41

10 × FWF → Toilets

DATE **Mon 28 Sep 2026**

TRUCK LEAVES

CARRIER

TORRENS 1

ON SITE

After 07:00

LOAD

Own page · no shared load
recorded

ON THE TRUCK

WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
10 × FWF Toilets · Toilets & amenities		None on the schedule

WHERE IT GOES

LOCATION	Toilets
SECTOR	S11
NEXT TO	
NEAR	S11 (~40 m)
CALLOUT	WC41 on D023-26003-02
BESIDE	
DOOR FACES	




MASTER-PLAN POSITION
-27.984821, 153.426070
From master plan D001 · not a
phone pin
SCAN TO NAVIGATE

PHOTOS



Master plan

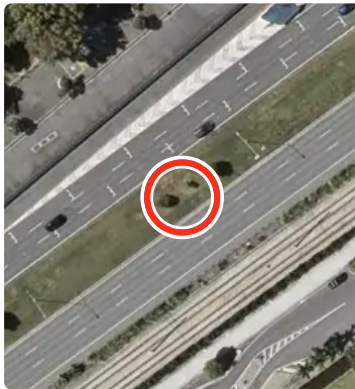

Close-up



Around it



The product · stock photo

INSTALL LIST

- | | | |
|---|--|---|
| ☐ Unload portaloos | ☐ Forklift work | ☐ Spotting |
| ☐ Arrival recorded in the page | ☐ Photos uploaded to the page | ☐ Asset numbers recorded in the page |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher **0429 352 788** INSTALLER Aaron Zelvis **0429 493 057** INSTALLER Alfie Harris **0403 149 326**
INSTALLER Kyle Gover **0403 789 142** IEDM SAFETY & TRAFFIC Steve Haines **0407 734 398** IEDM SITE MANAGER John Brett **0433 809 117**
EMERGENCY **000**

INSTALL

WC43

10 × FWF → Toilets

DATE **Mon 28 Sep 2026**

TRUCK LEAVES _____

CARRIER **TORRENS 1**ON SITE **After 07:00**LOAD **Own page · no shared load recorded**

ON THE TRUCK

WHAT	ASSET NO.	ACCESSORIES · TICK WHEN FITTED
10 × FWF Toilets · Toilets & amenities		None on the schedule


WHERE IT GOES

LOCATION	Toilets	
SECTOR	S14	CALLOUT WC43 on D023-26003-02
NEXT TO		BESIDE
NEAR	S14 (~20 m), Pit Lane (~50 m)	DOOR FACES




MASTER-PLAN POSITION
-27.986363, 153.427238
From master plan D001 · not a
phone pin
SCAN TO NAVIGATE

PHOTOS

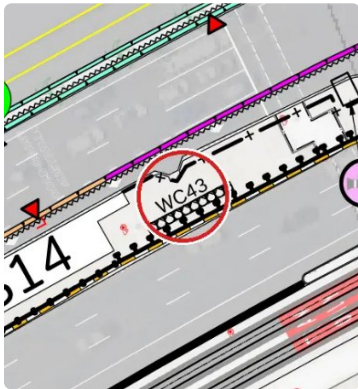

Master plan

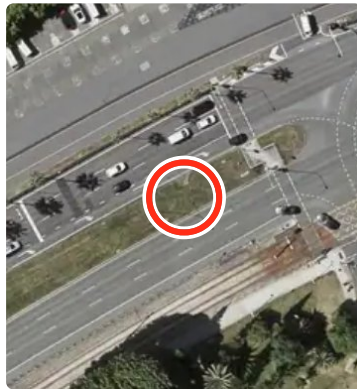

Close-up



Around it



The product · stock photo

INSTALL LIST

- | | | |
|---|--|---|
| ☐ Unload portaloos | ☐ Forklift work | ☐ Spotting |
| ☐ Arrival recorded in the page | ☐ Photos uploaded to the page | ☐ Asset numbers recorded in the page |

SAFETY

TAKE 5

Take 5 before every new task. Stop, look, assess, control, then proceed — before each new task and again whenever the job or conditions change (a new unit, a new position, a new crew member, weather, the public).

COATES LIFE SAVING RULES — read and followed on every task

Risk Assessment I will not commence any work that I am unfamiliar with, that is non-routine, potentially hazardous or impacted by changing conditions without first completing the appropriate Coates risk assessment tool to identify, assess and control risks.	High-Risk Work I will not commence any High-Risk Work without a risk assessment being completed and without having signed onto the applicable Safe Work Method Statement (SWMS).	Training and Competency I will be inducted, trained, competent and hold the required certification and licenses to conduct the task.
Fit for Work When I commence work, I will be physically fit, and not impaired by fatigue, injury, distraction, drugs or alcohol. I will wear the required personal protective equipment (PPE) as identified for the task or site rules.	Tools and Equipment I will only use tools and equipment that are fit for purpose and for which I am trained, competent and authorised. I will ensure that damaged or defective equipment is tagged out and removed from service.	Critical Risk Non-Negotiables When I commence a work activity related to a Coates Top 10 Critical Risk, I will always ensure that I review and strictly adhere to the non-negotiable rules and controls for that Critical Risk to protect me, my workmates and others from serious harm.

DOCUMENTS



Portable buildings and toilets, installation and removal
SEQ-SWMS-x TSV500.1
20 pages



Loading and unloading at third party sites
SEQ-SWMS-009.01g
34 pages

CONTACTS

COATES SITE Andrew Fisher **0429 352 788** INSTALLER Aaron Zelvis **0429 493 057** INSTALLER Alfie Harris **0403 149 326**
INSTALLER Kyle Gover **0403 789 142** IEDM SAFETY & TRAFFIC Steve Haines **0407 734 398** IEDM SITE MANAGER John Brett **0433 809 117**
EMERGENCY **000**
