BOOST MOBILE GOLD COAST 500 · 2026 BUILD

WHAT YOU BUILT

100% OF THE BUILD

Advanced Temporary Fencing — the fence crew on the Surfers Paradise street circuit, **Wed 9 September to Fri 23 October 2026**.

20.8 km

of fence and crowd control put in around the circuit, the grandstands, the compounds and the streets beside them — panel by panel, by hand.

20,797.5 m on the signed dockets: 13,270 m of fence, 7,257.5 m of crowd-control barrier and 270 m of flat feet.

TEMPORARY FENCE

13.3 km

13,270 m put in — **653 m more** than the programme asked for.

CROWD-CONTROL BARRIER

7.3 km

7,257.5 m — 2.2 km on the event lines, 5.1 km of demarcation, plus **270 m** of flat feet.

SCRIM

4.4 km

4,405 m of shade cloth — 3,977.5 m on braced fence, 427.5 m on fence already standing.

EVERY PIECE, CARRIED BY HAND

- **5,223** mesh panels
- **8,235** feet / bases on the dockets
- **7,977** clamps
- **1,426** braces
- **2,903** crowd-control barriers
- **133** vehicle gates
- **22** pedestrian gates
- **41** hoarding panels

Also: 117 flat-feet barriers and 278 gate wheels. Feet, bases and blocks are the same thing. Counted off the component boxes on the signed hire agreements.

THE CREW

SUPERVISOR

Wayne Woods

Advanced Temporary Fencing

- Owen Cowell McPaul
- Chase Hireni
- Scott Hildebrand
- Daniel Macleod
- Tahi Peni
- Hayden McAvoy
- Cody Woods
- Daniel Smith
- Alonzo McAvoy


"Fellas, this is what you built. 20.8 kilometres of fence and crowd control, put in by hand, in the wind and the rain — and done right. The public, the residents living right beside the circuit and V8 Supercars management had nothing but good things to say. Thank you."

Andrew Fisher · Coates · GC500 2026

From the signed dockets on the GC500 Delivery Control record, read 24 Oct 2026. Build: 9 Sep – Fri 23 Oct 2026. Demob still to come.

ADVANCED TEMPORARY FENCING · GC500 2026

THE BUILD, WEEK BY WEEK

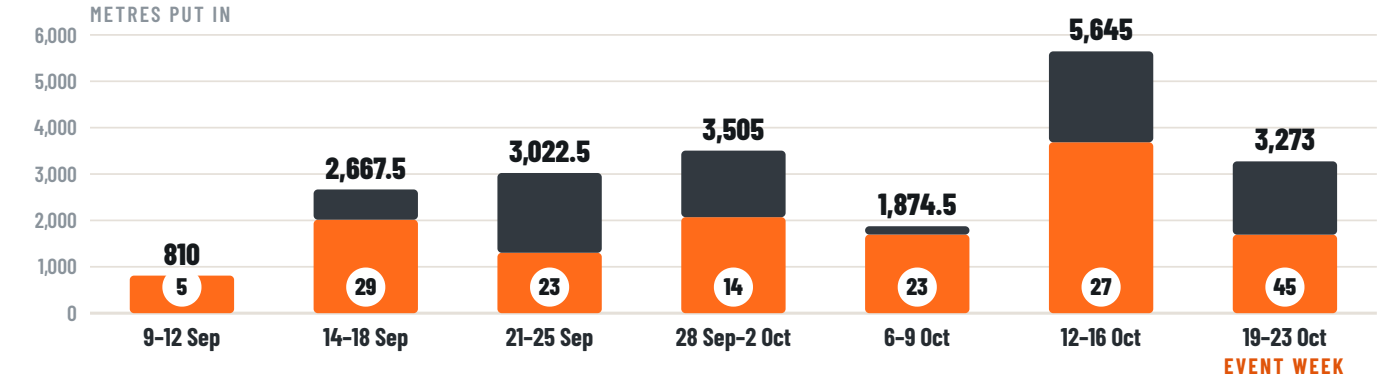

RECORD BREAKERS

BIGGEST WEEK

5,645 m

12–16 Oct: 3,685 m of fence and 1,960 m of crowd control in five days.

BIGGEST DAY

1,430 m

Mon 28 Sep, led by the Gold Coast Hwy median strip (north).

BIGGEST SINGLE JOB

1,210 m

Docket 36603, Tue 13 Oct: eastern residents and demarcation, Cable St to Gate 8A.


EVENT WEEK

45 dockets

In five days, 19–23 Oct. Thu 22 Oct alone: 15.

THE DETAIL

HOW THE FEET ADD UP



5,264 panels (incl. 41 hoarding) × 1 foot	**5,264**
1,426 braces × 2 feet	**2,852**
Dropped at the iEDM compound	**300**
Under flat-feet barriers, Club 500	**19**
From the gear (+1 at the end of each run)	**8,435+**

Every bracing docket shows two feet a brace, and a foot is shared at each panel join. **8,235** feet are written on the dockets, plus about **240** on the 10 papers that left the box blank: about **8,475 feet** used in all.

THE WORK YOU DO TWICE

Fence relocated when the plan moved	**612.5 m**
Taken down and stacked away	**1,102.5 m**
Put back up after a stack-down	**32.5 m**
Hours on service jobs (42 service notes)	**108.5 h**

BUILT THROUGH IT

113.6 mm
of rain over the build

18
wet mornings

15
days of gusts over 50 km/h

63 km/h
the big one, 7 Oct

Bureau of Meteorology, Gold Coast Seaway, 7 Sep – 23 Oct 2026. 65 mm fell in event week alone.

233 **signed papers**
over 32 working days on the dockets,
first in: Wed 9 Sep, Sea World Drive (36501)

166 hire agreements
42 service notes
25 collection forms

From the signed dockets on the GC500 Delivery Control record, read 24 Oct 2026. Fence and crowd control by the week the docket was written.
