
BOOST MOBILE GOLD COAST 500 · 2026 BUILD

WHAT YOU BUILT.

100% OF THE BUILD

Advanced Temporary Fencing
Wayne Woods and crew · Wed 9 Sep – Fri 23 Oct 2026

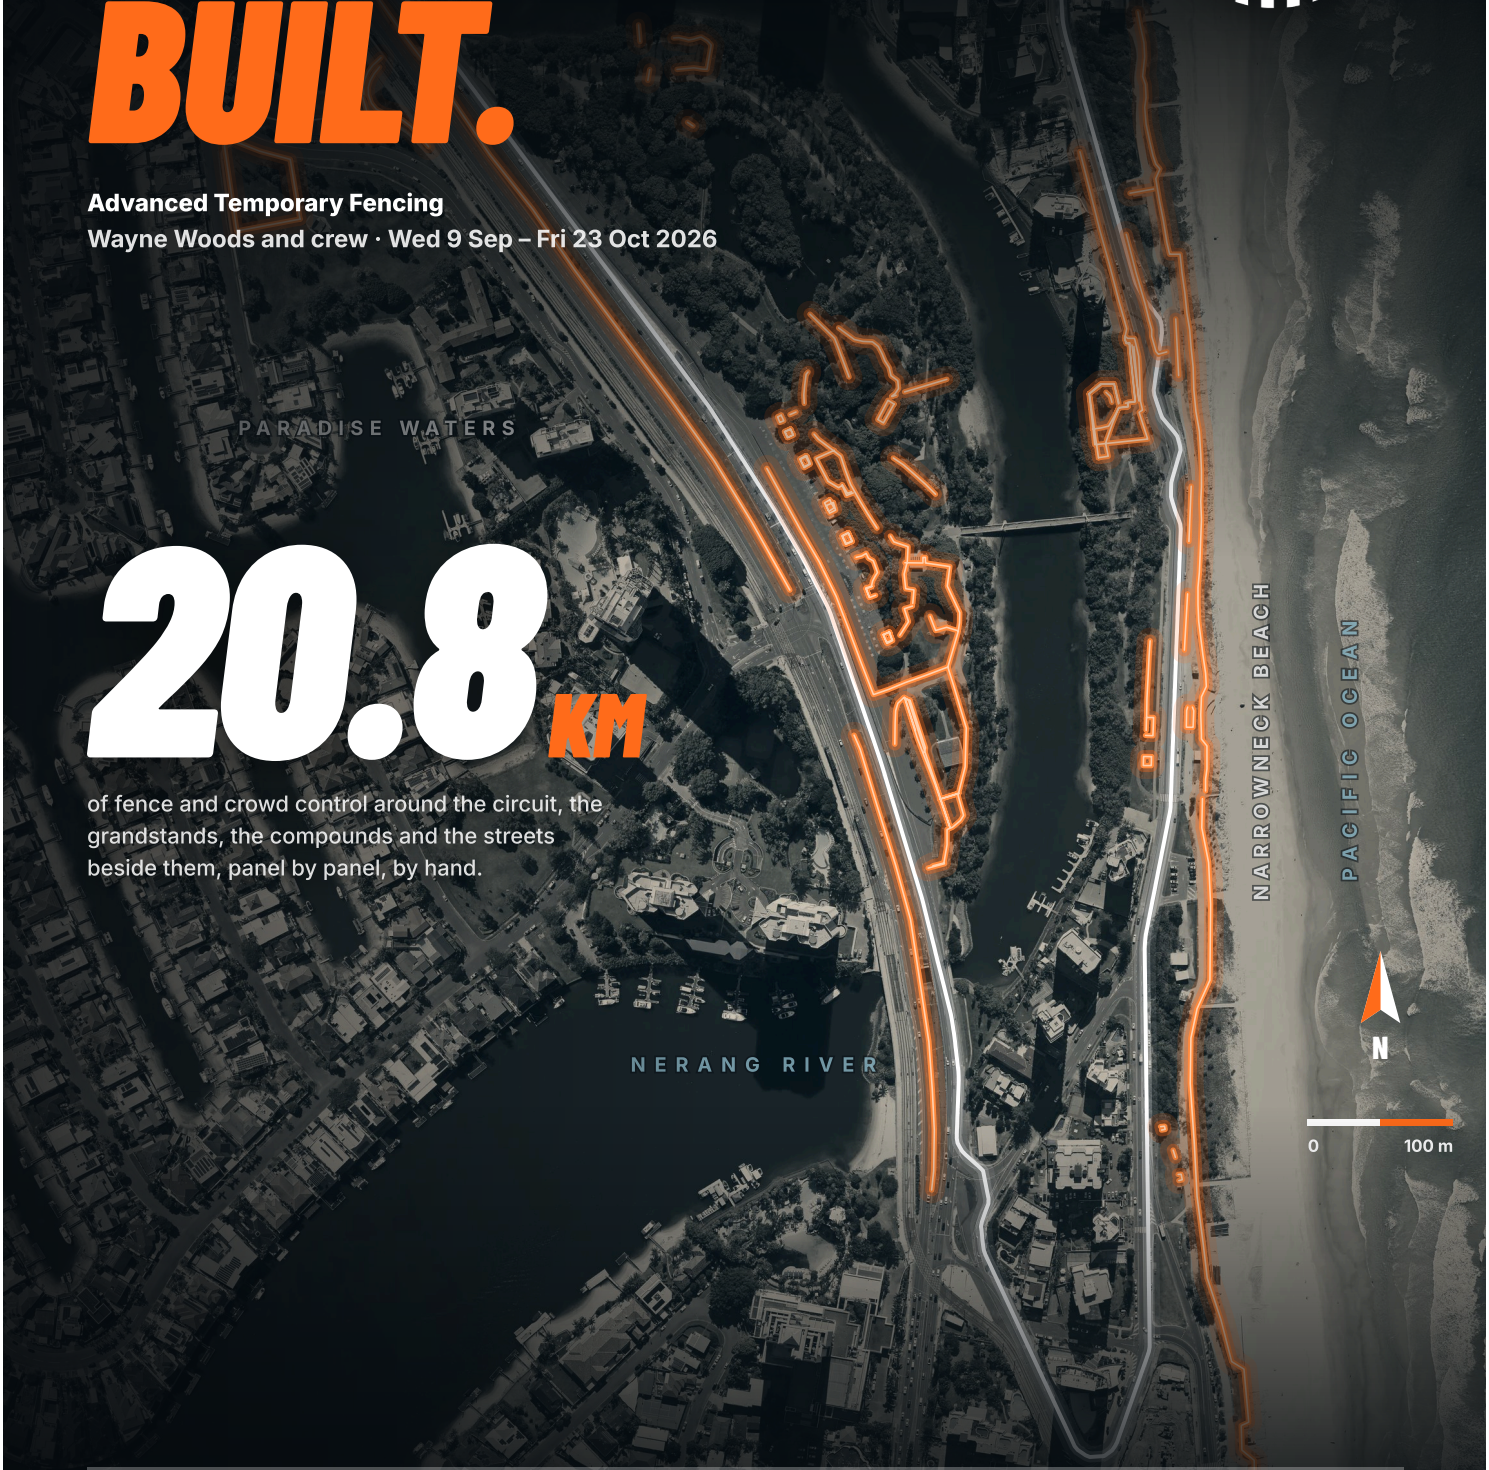

20.8 KM

of fence and crowd control around the circuit, the grandstands, the compounds and the streets beside them, panel by panel, by hand.

13.3 KM TEMPORARY FENCE

7.3 KM CROWD-CONTROL BARRIER

4.4 KM SCRIM

233 SIGNED PAPERS

Fence runs on the weekly installation plans — The track

© State of Queensland 2022 · CC BY 4.0 · 10 cm aerial, Jul 2022–Sep 2022 · Fence runs: the weekly installation plans traced onto iEDM's master plan D001-26003-03 (selected runs, not every panel) · Track: iEDM key plan K220-K231-26003-02 · Placed by the GC500 record's registrations, not surveyed

THE NUMBERS

EVERY PIECE, CARRIED BY HAND. 02

TEMPORARY FENCE

13.3 KM

13,270 m put in, **653 m more** than the programme asked for.

CROWD-CONTROL BARRIER

7.3 KM

7,257.5 m: 2.2 km on the event lines and 5.1 km of demarcation, plus **270 m of flat feet**.

SCRIM

4.4 KM

4,405 m of shade cloth: 3,977.5 m on braced fence and 427.5 m on fence already standing.

END TO END

20.8 KM WOULD GO ROUND THE STREET CIRCUIT MORE THAN SEVEN TIMES.

One lap is 2.91 km on the record's registered key plan: 20,797.5 m ÷ 2,910 m = 7.15 laps.



THE GEAR, COUNTED OFF THE SIGNED PAPERS

each symbol is 100

8,235
FEET / BASES
feet, bases and blocks: the same thing

7,977
CLAMPS
holding the panels together

5,223
MESH PANELS
plus 41 hoarding panels

2,903
CROWD-CONTROL BARRIERS
2.2 km of event lines, 5.1 km of demarcation

1,426
BRACES
two feet under every one


133	22	41	117	278
VEHICLE GATES	PEDESTRIAN GATES	HOARDING PANELS	FLAT-FEET BARRIERS	GATE WHEELS

Counted off the component boxes on the 166 signed hire agreements. Feet, bases and blocks are the same thing: 8,235 are written on the papers, and about 8,495 were used, counting the 11 papers that left the feet box blank. The dockets show two feet under every brace and one at every panel join.

SEVEN WEEKS

THE BUILD, WEEK BY WEEK.


03

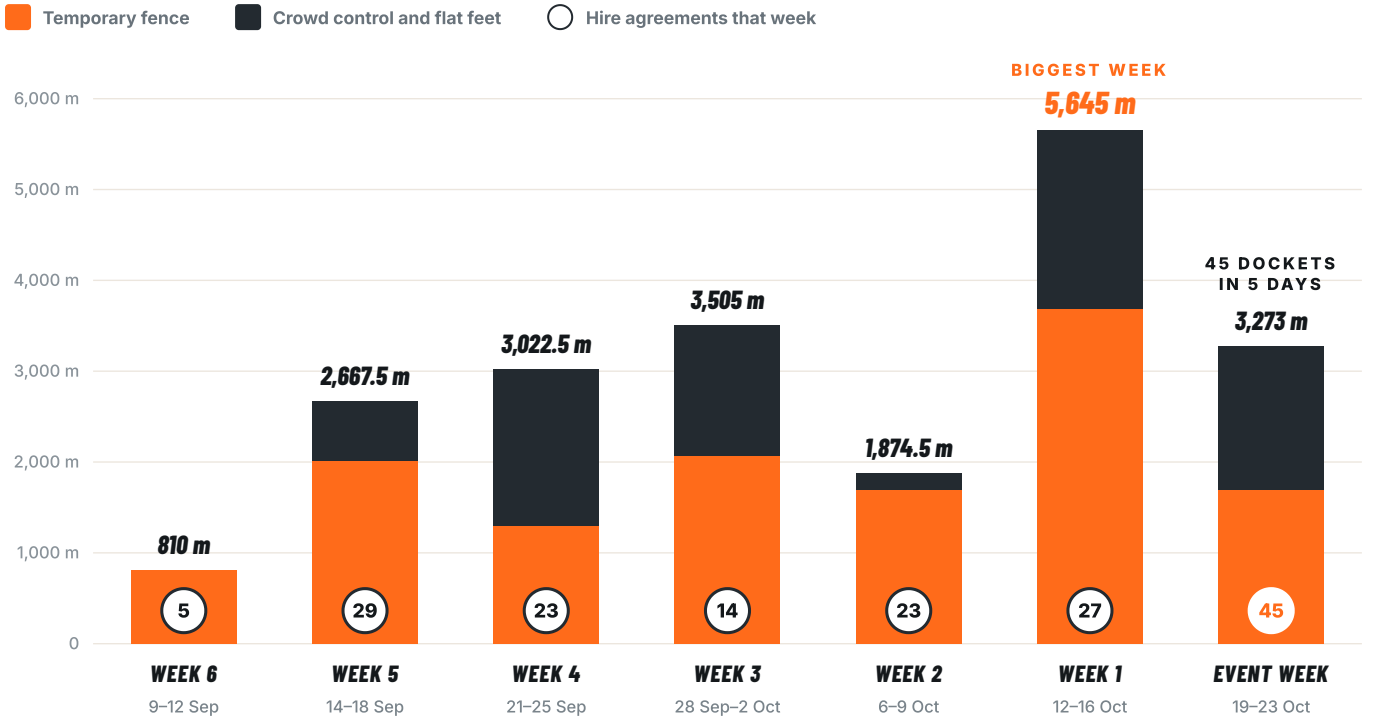

THE RUNNING TOTAL

10 km by Fri 2 Oct

20.8 km by Fri 23 Oct



BIGGEST WEEK

5,645 m

12–16 Oct: 3,685 m of fence and 1,960 m of crowd control in five days.

BIGGEST DAY

1,430 m

Mon 28 Sep, led by the Gold Coast Hwy median strip (north).

BIGGEST SINGLE JOB

1,210 m

Docket 36603, Tue 13 Oct: eastern residents and demarcation, Cable St to Gate 8A.

EVENT WEEK

45 dockets

In five days, 19–23 Oct. Thursday 22 Oct alone: 15.

BUILT THROUGH IT

113.6 mm
of rain

18
wet mornings

15
days of gusts over 50 km/h, six in a row 14–19 Oct

63 km/h
the big gust, 7 Oct

65 mm
in event week alone

12.9° to 29.9°
coldest morning 27 Sep, hottest day 12 Oct

Bureau of Meteorology, Gold Coast Seaway, 7 Sep – 23 Oct 2026 (rain to 9 am).

THE WORK YOU DO TWICE

612.5 m	of fence moved when the plan moved
1,102.5 m	taken down and stacked away
32.5 m	put back up after a stack-down
108.5 h	on service jobs, over 42 service notes

233 SIGNED PAPERS

166 hire agreements · 42 service notes · 25 collection forms, over 32 working days. First in: Wed 9 Sep, Sea World Drive (36501).

Metres by the week the docket was written · From the signed papers on the GC500 Delivery Control record, read 24 Oct 2026

THE CREW

THE LINE-UP.

04

WW

SUPERVISOR

WAYNE WOODS

Advanced Temporary Fencing

OM OWEN COWELL MCPAUL	DM DANIEL MACLEOD	CW CODY WOODS
CH CHASE HIRENI	TP TAHI PENI	DS DANIEL SMITH
SH SCOTT HILDEBRAND	HM HAYDEN MCAVOY	AM ALONZO MCAVOY

Fellas,

This is what you built. 20.8 kilometres of fence and crowd control around the Surfers Paradise street circuit: every panel, every foot and every clamp carried and stood up by hand, in the wind and the rain, and done right.

You finished the build. One hundred per cent, ready for race weekend. And from the public, the residents living right beside the circuit and V8 Supercars management: nothing but positive feedback.

That's how you represent a job. Thank you.

ANDREW FISHER

Shutdown Manager · Coates · GC500 2026

BUILD COMPLETE

100% · FRI 23 OCT 2026

Author: Andrew Fisher, Coates · Names and company as the crew's sign-on sheet reads · From the GC500 Delivery Control record, read 24 Oct 2026 · Map imagery © State of Queensland 2022, CC BY 4.0
