



COATES INDUSTRIAL SOLUTIONS • BOOST MOBILE GOLD COAST 500

GC500 Delivery Control

One live record for the whole build, from the truck leaving the yard to the last unit being numbered on site. Every delivery, every dollar and every hour of labour, on one map that anyone on the job can open.

BEST SERVICE & VALUE

Author: Andrew Fisher

Shutdown Manager

As at Tue 29 Sep 2026 • Week 3 of the build
24 days to race day

Built the Coates Way

A street circuit is a big build in a short window: **789 units across 10 trades on 198 references**, fencing crews, carriers and a race date that doesn't move. We built GC500 Delivery Control so everyone works from the same picture, and so the customer gets what they ordered, where they need it, when they need it.

CARE DEEPLY

The daily pre-start is prefilled from the record and linked to the SWMS. The install crew get a sheet with photos and the exact spot, so there's less guessing on the road and on the tools.

CUSTOMER FOCUSED

Every reference shows what was asked for and what was supplied. A short delivery is flagged straight away, and the rest of the order can be booked onto another day.

BE OUR BEST

Every figure comes from one record. When something isn't known, the page says "not recorded" rather than guessing.

ONE TEAM

Drivers, installers and the branch all see the same live record. The view link is read-only, so it's safe to share.

COMPETITIVE SPIRIT


A race-day countdown on every page, and a Showcase that shows the customer the build in 3D, day and night.



The Coates Way machine inside the dashboard. Best Service & Value is the centre cog, and every part connects back to it.

A nice touch: every day on the Timeline carries one of the five values in turn, so the crew see them each time they check their loads.

On plan, and we can prove it

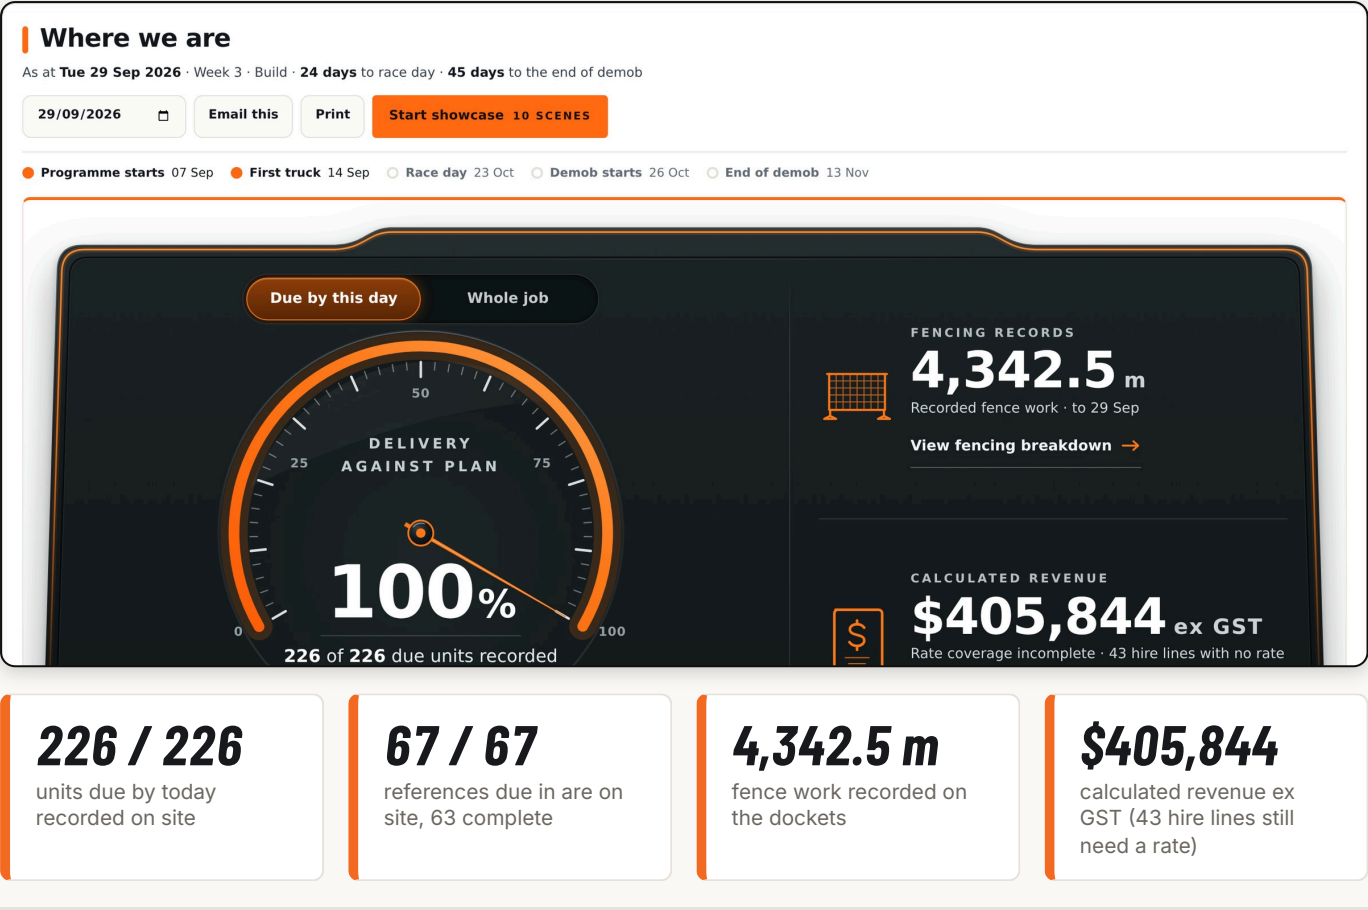

The master plan, laid on the real world

☰

Coates Industrial Solutions | GC500 2026

Satellite Plan Explorer · D001 rev 03 · Master Layout Plan

Original plan

Satellite + plan

Satellite only

SEARCH THE MASTER PLAN AND THE DRAWING

WC69, P12, S08, an asset number, a

FIND ON THE MASTER PLAN

Access & plant 2

Furniture 4

Generators 12

Ground protection 1

Lighting towers 13

Portable buildings 52

Toilets & amenities 68

Water-filled barriers 12 locations · 20 runs

VMS boards 19

Gates 19

Entry points 23

Big screens 13

Other gensets 9

Interface areas 4

Drawn, not on our schedule 7

Stands 20

Bars 8

Armco access 51

Emergency egress 2

Over-track signage 5

Pedestrian bridges 3

Full master plan · as drawn

100%

-

+

Fit

☐

PNG

N

E

S

W

Facing east


As drawn

Source detail rendered · last tile 624 ms


© Mapbox © OpenStreetMap © Maxar · Drawing © iEDM D001 rev 03

- **Every trade, one screen:** the D001 Master Layout Plan lined up on satellite imagery of the whole circuit, from Main Beach to Surfers Paradise.
- **Find by trade:** a chip per trade with its count. Toilets (68), portable buildings (52), gates (19), VMS boards (19) and more light up where they stand.
- **Search anything:** a reference, a name, an asset number or a callout. It flies straight there.
- **Original plan, Satellite + plan, or Satellite only,** with a compass, zoom down to the metre and a PNG export.

Every reference, right where it sits

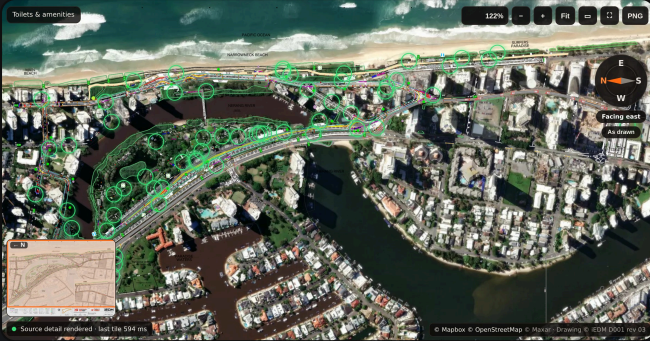

Toilets & amenities: every toilet on the job, ringed on the plan.

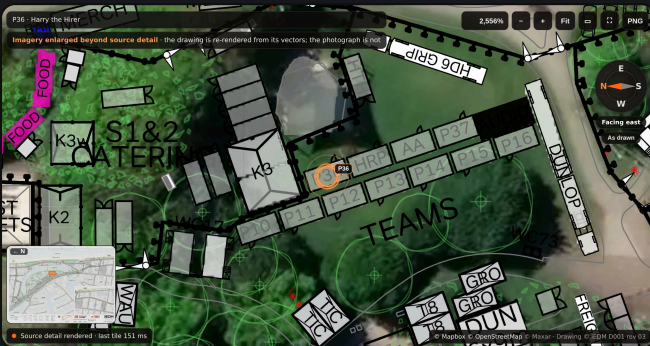

Zoomed to 2,556%: P36 found by search, among the team buildings.



The pit lane and paddock, with pins along the circuit.



WC41 found by search: the plan drawn crisp over the street, down to the lane markings.

100

photos on 37 references so far, with more added every day

24

references pinned on the ground by phone, where they actually sit

- **Photos on every reference:** the crew photograph each unit as it goes in. The photos sit on its record, its card and its driver and install sheets.
- **Pinned where it really is:** the pin is dropped on site from a phone, not guessed from the drawing, so everyone knows exactly where they're going.
- **Navigate:** one tap for Google Maps directions to that spot, driving or walking.
- **3D mode:** 366 pins on the model, checked against the master plan to within 0.1 m, with named views and an Ultra (4K) setting.

Every truck, every day, one line each

DUE IN (9) · 7 LOADS

LOAD 1	09:00 SFL	P38 NO RECORD Building 6m	Green Room 1
LOAD 2	09:30 SFL	P39 NO RECORD Building 6m	Green Room 2
LOAD 3	10:00 SFL	P42 NO RECORD Building 6m	Production
LOAD 4	10:30 SFL BOGIE	GN01 NO RECORD 60kva WC01 NO RECORD Accessible Toilet, FWF x2 WC42 NO RECORD FWF	near S13 +2
LOAD 5	10:30 SFL	P06 NO RECORD Building 6m	Wiltclean Crib Room
LOAD 6	— TORRENS 1	WC41 NO RECORD FWF x10	near S11
LOAD 7	— TORRENS 1	WC43 NO RECORD FWF x10	near S14

Coates Industrial Solutions · GC500 · Author: Andrew Fisher · built 2026-09-25 · assets-1.0.0

Shared record · live · view only — this link cannot change it · last confirmed 21:43

A delivery day: one line per load with the time, the carrier, the references on the truck and where they're going. Tap a line to open it.

- **Every day of the programme, 07 Sep to 13 Nov:** what's due in and out, the loads on the carrier's list, and how many are recorded on site.
- **Day documents** sit on every day: **Pre-start, Drivers, Install, Email** and **Edit**.
- **Email** attaches the PDFs themselves, one per load, with no links, ready to go from a phone.
- **Change deliveries:** move a reference to another day, record what turned up, or cancel an order with the reason kept.
- **Short deliveries are flagged:** for example, "WC01: Accessible Toilet 0 of 1". The rest of the order can be booked on a later day, and the money is never counted twice.

15

references due in the next 7 days

23 Oct

race start. The countdown is on every page.

The right sheet in the right hands

Coates INDUSTRIAL SOLUTIONS DELIVERY DRIVER SHEET - GC500-DRV-01
Delivery - Mon 28 Sep 2026

GC500-DRV-01
LOAD 1 OF 7

DELIVER

P38
1 x Building 6m - Green Room 1

DATE: Mon 28 Sep 2026
LOAD TIME: 09:00 Kingston
CARRIER: SFL
ON SITE: After 07:00
LOAD: One truck - one ref

ON THE TRUCK
WHAT: 1 x Building 6m
ASSET NO.: 1327218
FRIDGE (Full Size)

WHERE IT GOES
LOCATION: Green Room 1
SECTOR: P39, P42
STAGE: Macintosh Island (~75 m)
FROM DATE: south-east, about 480 m
WAY IN: Sundale Bridge - Tedder Ave Access Point, gate G10
ESCORT: Do not drive through the park unescorted

PHOTOS
Whole site From the road Close-up Master plan

SAFETY
PPE: Hi-vis, safety glasses, steel-cap boots Site hours 07:00-17:00 Monday to Friday

TAKE 5
Take 5 before every new task. Stop, look, listen, control, then proceed - before each new task and again whenever the job or conditions change to new unit, a new position, a new crew member, weather, the public.

COATES LIFE SAVING RULES - read and followed on every task

Risk Assessment
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

High Risk Work
I will not commence any high risk work without a risk assessment being completed and signed off by the applicable Safe Work Method Statement (SWMS).

Fit for Work
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

Safe Transport of Portable Buildings
I will ensure that the portable building is loaded and secured in accordance with the applicable Safe Work Method Statement (SWMS).

Pre-Transit Checklist - Site Accommodation Work
I will ensure that the portable building is loaded and secured in accordance with the applicable Safe Work Method Statement (SWMS).

Guidance sheet for lifting portable buildings
I will ensure that the portable building is loaded and secured in accordance with the applicable Safe Work Method Statement (SWMS).

CONTACTS
COATES SITE: Andrew Fisher 6429 352 788 COATES OFFICE: Ross Saxby (07) 3299 9797 IEM SAFETY & TRAFFIC: Steve Holmes 6407 734 398
IEM SITE MANAGER: John Brett 6433 899 117 EMERGENCY: 888

Coates Industrial Solutions - GC500-2026- Author: Andrew Fisher

Coates INDUSTRIAL SOLUTIONS INSTALL TEAM SHEET - GC500-INS-01
Install - Mon 28 Sep 2026

GC500-INS-01
LOAD 1 OF 7

INSTALL

P38
1 x Building 6m - Green Room 1

DATE: Mon 28 Sep 2026
TRUCK LEAVES: 09:00 Kingston
CARRIER: SFL
ON SITE: After 07:00
LOAD: One truck - one ref

ON THE TRUCK
WHAT: 1 x Building 6m
ASSET NO.: 1327218
FRIDGE (Full Size)

WHERE IT GOES
LOCATION: Green Room 1
SECTOR: P39, P42
STAGE: Macintosh Island (~75 m)
FROM DATE: south-east, about 480 m
WAY IN: Sundale Bridge - Tedder Ave Access Point, gate G10
ESCORT: Do not drive through the park unescorted

PHOTOS
Master plan Close-up Around it The product - stock photo

INSTALL LIST
☐ Unload a building (crane)
☐ Fit stairs and landings
☐ Position and level a building
☐ Power-on check with the electrician
☐ Spitting
☐ Forklift work
☐ Photos uploaded to the page

SAFETY
TAKE 5
Take 5 before every new task. Stop, look, listen, control, then proceed - before each new task and again whenever the job or conditions change to new unit, a new position, a new crew member, weather, the public.

COATES LIFE SAVING RULES - read and followed on every task

Risk Assessment
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

High Risk Work
I will not commence any high risk work without a risk assessment being completed and signed off by the applicable Safe Work Method Statement (SWMS).

Fit for Work
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

Safe Transport of Portable Buildings
I will ensure that the portable building is loaded and secured in accordance with the applicable Safe Work Method Statement (SWMS).

Pre-Transit Checklist - Site Accommodation Work
I will ensure that the portable building is loaded and secured in accordance with the applicable Safe Work Method Statement (SWMS).

Guidance sheet for lifting portable buildings
I will ensure that the portable building is loaded and secured in accordance with the applicable Safe Work Method Statement (SWMS).

CONTACTS
COATES SITE: Andrew Fisher 6429 352 788 INSTALLER: Aaron Zehav 6429 493 857 INSTALLER: Alfa Harris 6403 149 326
INSTALLER: Kyle Gover 6403 789 142 IEM SAFETY & TRAFFIC: Steve Holmes 6407 734 398 IEM SITE MANAGER: John Brett 6433 899 117 EMERGENCY: 888

Coates Industrial Solutions - GC500-2026- Author: Andrew Fisher

- One A4 page per load, made from the record: the reference in big type, what's on the truck, its photos, and a close-up of the plan with the drop point pinned where it really is.
- Scan to navigate: each drop has a QR code that opens directions to the exact spot. All 483 of 483 codes were tested and scan.
- Installers get the same load with what goes where and the notes they need for the install.
- Pre-starts come prefiled for the days ahead on the current Coates Installs form, linked to the SWMS, then printed, signed and uploaded against that day.

Daily pre-start - Mon 28 Sep 2026 - 1 page

Coates INDUSTRIAL SOLUTIONS BUILDINGS & TOILETS - INSTALLERS
GC500-2026
SUPERVISOR: JOHN BRET
SUNDALE PARK, SUNDALE PARK

Coates Install Team
01 THE DAY
Mon 28 Sep 2026
Coates Installs

02 HOW THE DAY WILL RUN
Traffic and the day: I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

03 THE WORK
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

04 THE LOADS ON THIS DAY
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

05 HAZARDS AND CONTROLS
I will not commence any work that I am not competent to do, that is not within my training, experience and without having signed off the applicable Safe Work Method Statement (SWMS).

Are we making money? An honest answer

Are we making money?

as at Tue 29 Sep 2026 · AUD ex GST

Revenue is what Coates charges the V8s — everything on hire is revenue. A **direct cost** is what Coates pays for the job, named by its Coates P&L line where the record shows which line it is. The two are never added together.

\$405,844

REVENUE

\$218,803

DIRECT COSTS — KNOWN SO FAR

\$187,041

DIFFERENCE SO FAR

6

NOT IN IT YET

STREAM	REVENUE	DIRECT COSTS	DIFFERENCE	STILL TO COME
Fencing Advanced Temporary Fencing — revenue at the 2026 card, hire and installation in one rate · direct costs at their own sheet: Rehire (their gear) and Installation — external contractors (their crew)	\$92,551	\$61,427	\$31,124	58 dockets · Rehire \$59,627 (their gear) · Installation — external contractors \$1,800 (their crew) · green-book labour 9.5 h
Toilets and servicing Event Portables rehire — revenue at our rates · Rehire cost, paid to Event Portables	\$69,092	\$118,575	-\$49,483	Rehire cost: Event Portables \$118,575, approved — the final total may change · 7 of 132 contract lines with no rate yet — the charge for them is missing · servicing is on no contract line: the same servicing at our card's pump-out rates would be \$85,102 — not charged yet
Buildings, containers and furniture our own fleet (KINP)	\$66,992	—	\$66,992 before direct costs	3 of 88 contract lines with no rate yet — the charge for them is missing · 1 subhired line — its rehire cost is not on the record
VMS, water barriers and track mat our own fleet (STPS)	\$81,149	—	\$81,149 before direct costs	
Forklifts and access MEAD and NVAC	\$15,935	—	\$15,935 before direct costs	10 of 15 contract lines with no rate yet — the charge for them is missing · 1 subhired line — its rehire cost is not on the record
Generators and lighting towers NVAC	\$339	—	\$339 before direct costs	23 of 24 contract lines with no rate yet — the charge for them is missing
Delivery and transport Transport Revenue: the delivery and pickup lines on the contracts · Transport (cartage): paid to the carriers	\$6,939	\$21,721	-\$14,782	Transport (cartage): the schedule's TPORT COST figures — only the loads with a figure, the 7 fencing semis to Phillip Park among them (\$8,637; Coates organises their transport) and 6 loads with no reference (\$2,553) · Transport Revenue: the delivery and pickup lines on the contracts; for comparison, the 2026 card's transport charge for the

Coates Industrial Solutions · GC500 · Author: Andrew Fisher · built 2026-09-25 · assets-1.0.0

Shared record · live · view only — this link cannot change it · last confirmed 08.09

Revenue (what Coates charges) and direct costs (what Coates pays) are kept apart, stream by stream, and never added together.

\$405,844

revenue, ex GST

\$218,803

direct costs known so far

\$187,041

difference so far. Not a margin yet: 6 items aren't in it.

- **Labour ticked per piece:** each unit carries its expected labour, and a tick charges it. That's 162 ticks so far, worth **\$17,031**, with \$6,517 on site ready to tick and \$21,528 to come.
- **Event labour scope:** \$55,817, made up of 368.9 h of people plus \$19,102 of accommodation and travel.
- **Hours tracked:** 2,168 h on the tracker, split into ordinary time, ×1.5, ×2 and race weekend, for our crew and our labour-hire contractors.
- **Direct costs** go against the eight categories management expect, with the P&L line where the record shows it: rehire, fencing, transport, accommodation and meals.
- **It shows where money could be missing:** servicing isn't on any contract line. At our card's pump-out rates it would be **\$85,102**, not charged yet. And 43 contract lines still have no rate.

Every figure is worked out from the record, and it's clearly marked where the forecast is incomplete. For example, crew wages are in hours only until a wage rate is added.

What's on site, whose it is, and where it sits

Inventory - on site now Tue 29 Sep 2026 · from the delivery record, so it moves as things are ticked on site

Sub-hired on site: **Event Portables 1** on site (1 at locations)

TOILETS & AMENITIES
EVERYTHING
ACCESS & PLANT
FURNITURE
GENERATORS
GROUND PROTECTION
LIGHTING TOWERS
OTHER
PORTABLE BUILDINGS

VARIABLE MESSAGE SIGNS
WATER-FILLED BARRIERS

TYPE	TOTAL ON SITE	SUB-HIRE	SPARE	AT LOCATIONS	COATES NUMBERED	NO NUMBER YET	STILL TO COME	ORDERED
16Pan Block	2	-	0	2	0	2	0	2
Accessible Toilet	2	-	0	2	0	2	2	4
FWF	62	Event Portables 1	0	62	40	21	167	229
FWF Trailer	2	-	0	2	2	0	0	2
Pee Panel	0	-	0	0	0	0	6	6
Toilet Block 6m	9	-	0	9	9	0	6	15
Waste tank	2	-	0	2	0	2	2	4
Total	79	1	0	79	51	27	183	262

Press any number to see which locations are behind it. Total on site = at locations + spares. At locations: the order's quantity once it is ticked on site (or what was recorded as supplied). A location with two types counts its numbers against its biggest line. Cancelled orders are not counted.

Inventory on site now, Toilets & amenities: 262 ordered, 79 on site, 51 carrying a Coates number and 1 Event Portables unit already recorded. Tap any number to see the locations behind it.

- **Stock by type and by trade:** ordered, at locations, Coates-numbered, sub-hired by company, spares, and still to come.
- **Spares:** units on site that aren't at a location. Each spare can be sent to a location, or taken off when it leaves site.
- **Swap:** change a Coates unit for a sub-hired one (or the other way round) in one step. What comes out goes back to spares.
- **Walk-around:** type the sticker number, press Enter, and it moves to the next location that still needs a number. A duplicate is refused and the page names where the number already is.
- **What turned up:** count each item against the order. Short and extra are flagged everywhere they matter.
- **Cancel an order:** it comes off every count, list and sheet, keeps the reason, and can be put back with one press.

The build, told like race day. Day and night.



Race day in daylight: the Coates #26 on the pit straight (Ultra setting), the start gantry and grandstand crowd from the drone, the whole circuit from the air, and the car at speed past the pit boxes. Switch the backdrop to night and the city lights up.

- **Ten scenes, one button:** press Start showcase on "Where we are". It runs hands-free, or one scene at a time.
- **A real circuit:** built from the event key plan and OpenStreetMap buildings, with the pit lane, kerbs, grandstands and crowd.
- **Day or night:** switch the backdrop and the whole circuit changes with it, from sunlight to the city lit up after dark.
- **Crisp on a 4K screen:** the Ultra setting draws up to 6 million pixels a frame, with 4× anti-aliasing and sharper shadows, so it holds up on a boardroom TV.
- **The figures are live:** every number in the scenes is read from the record as it stands on the day.

BROADCAST · TURN THE SOUND UP

A 35-part live race call voiced like Supercars commentary. There's a lead caller and a colour commentator, with the crowd and a V8 underneath, calling our build as if it's race day.

COATES FM · ON THE RADIO

Climb into the Coates Way machine and press RADIO on the steering wheel for a Coates FM segment with a radio host. It's tuned like a car radio, and the V8 drops back while it plays.

The power behind performance



The Coates Way, built as a race car. Best Service & Value is the centre cog, and the performance pillars, scorecard and behaviours are the parts that drive it. Every part is connected, so you can see what makes it run.

- **310 parts**, each named for a part of the Coates Way. Tap one to see what it does.
- **From the driver's seat**: the steering wheel runs everything. There's Start V8, throttle and brake, and 26 controls that click and move.
- **Coates FM**: press RADIO on the wheel for a Coates FM segment with a radio host. It has car-radio sound, and the V8 drops back while it plays.
- **Explode the powertrain**, cut it away, or follow the power path from the centre cog out to the wheels.
- A guided tour and a built-in **4K capture** button, in a working garage with a gantry crane, a hoist and tyre machines.



Frames captured at 3840 px: the #26 in the garage with the cutaway on, the driver's seat with the Coates Way on the wheel, and the V8 powertrain in the dyno cell.

Why the business can trust it

- **One source of truth:** every tab reads the same live record, so the numbers match everywhere.
- **Honest by design:** "not recorded", "assumed" and "differs" are shown as different things, and nothing is estimated and passed off as fact.
- **Accountable:** every change carries who made it and when.
- **Safe to share:** the view link is read-only. Only the site team can edit.
- **Works where we work:** phone, tablet or desktop. It prints to A4 and emails PDFs.
- **Tested before it goes live:** every change is checked on desktop and phone against the live data before it's released.

WHERE IT COULD GO NEXT (FOR DISCUSSION)

- Carry it through demob to 13 Nov, with every unit numbered off site.
- Get rates on the 43 unrated contract lines, and sort out the servicing charge with the branch.
- Use the same approach on other events and shutdowns: live deliveries, labour and costs, on a map.

HAVE A LOOK (VIEW ONLY)

gc500-production.up.railway.app/v/Coates-GC500-2026

Open Map explorer, then press Start showcase on "Where we are", with the sound on.

Thanks to the crew and the drivers who keep the record right on the ground. The tool is only as good as the people using it, and they've been brilliant.

Andrew Fisher · Shutdown Manager
